
Communications Tree

Yosemite Village · Who talks to whom, how often, and where problems go

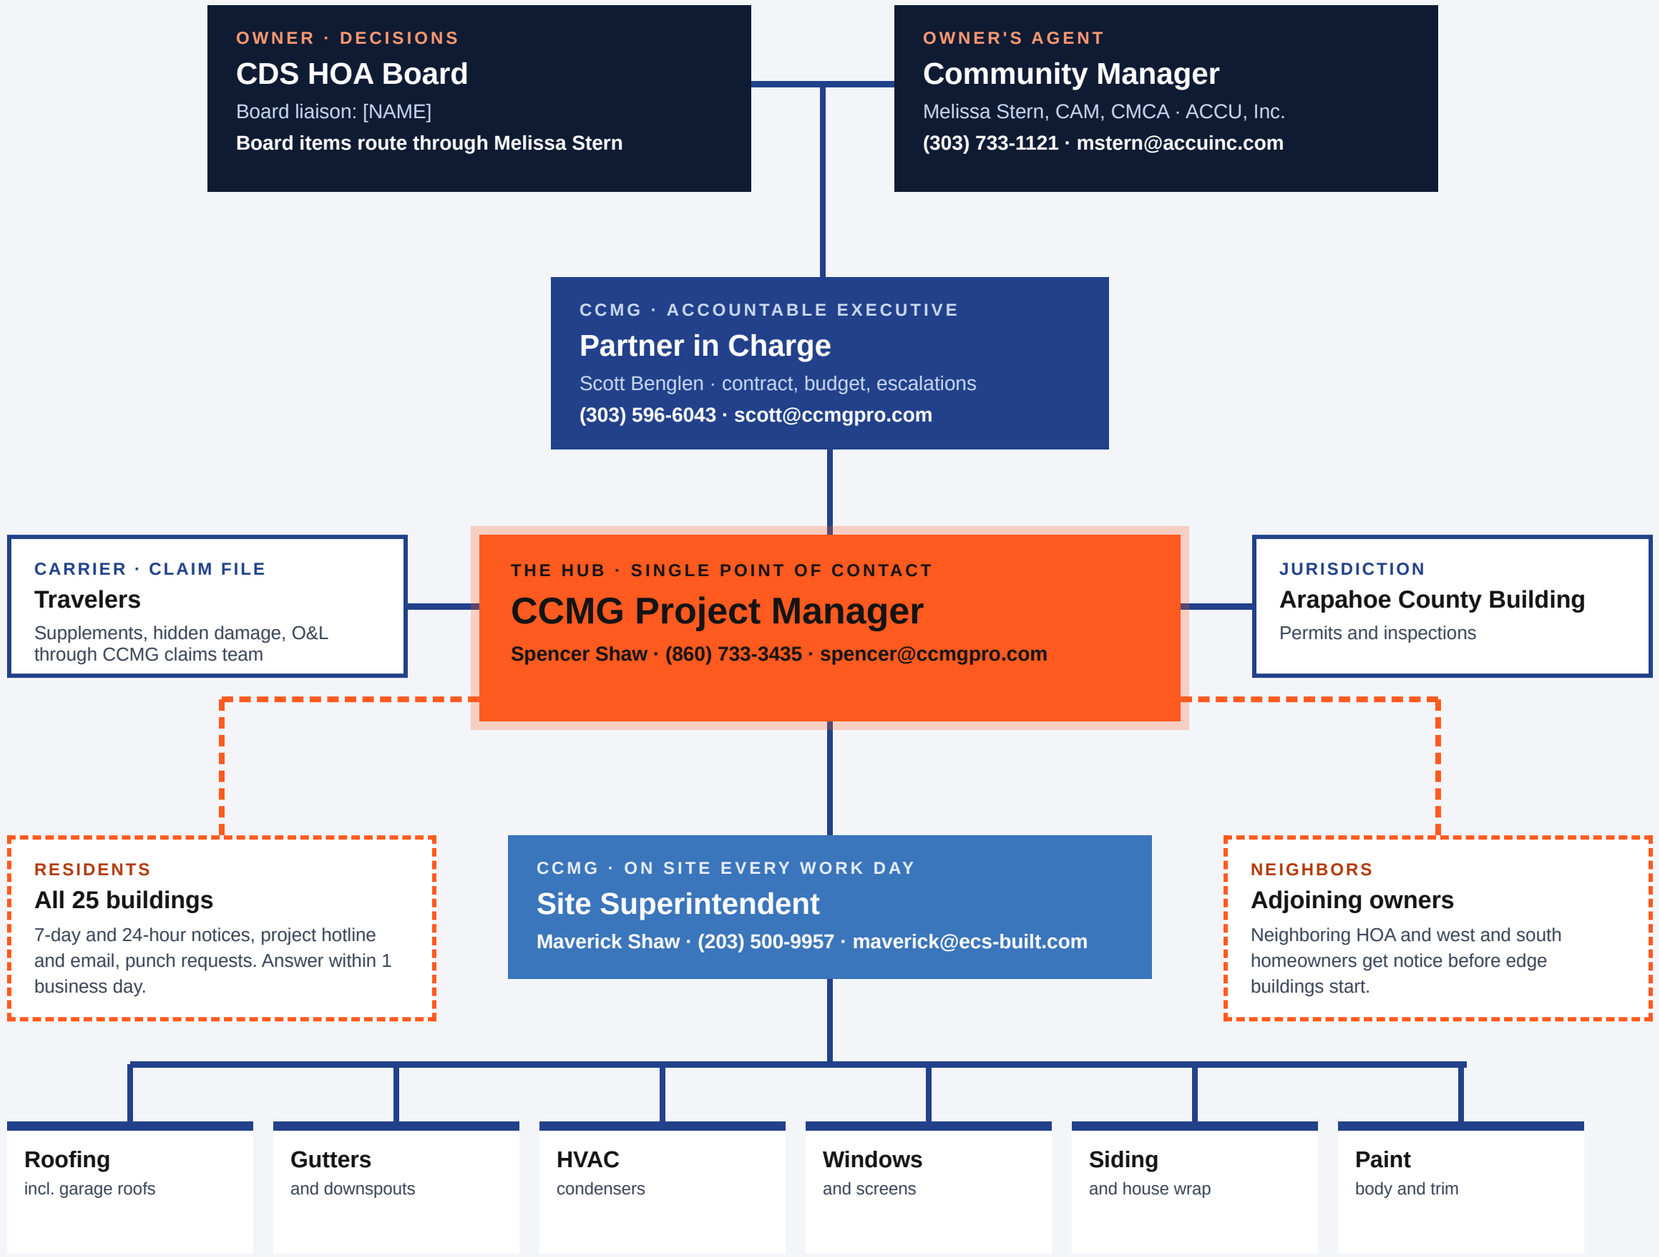

Trade subs report to the Superintendent through one bus. Nobody below the Project Manager talks scope or money with the board, the manager or residents.

CADENCE

DAILY	Superintendent huddle with trade leads. Site sweep. Next-day notice check.
PER BUILDING	7-day and 24-hour resident notices from the PM. Manager reposts.
WEEKLY	Written update to board and manager: buildings closed, next week's buildings, open issues, photos.
EVERY 2 WEEKS	Progress meeting: board liaison, manager, CCMG PM. Decisions logged.
PER DRAW	Draw request with progress photos and lien waivers to the board treasurer.

ESCALATION LADDER

1. **Superintendent.** Resolve on site the same day.
2. **Project Manager.** Written answer within 1 business day.
3. **Partner in Charge.** Within 2 business days.
4. **Board.** Through the manager, at the next meeting or sooner.

EMERGENCY · INJURY · LEAK · PROPERTY DAMAGE

Call 911 if anyone is hurt. Superintendent secures the area and calls the PM. PM notifies the Partner and the manager within 1 hour, and the board president the same day. Written incident report within 24 hours.

THREE RULES

One voice. Every resident notice comes from the CCMG PM. The manager reposts, never rewrites.

Nothing changes verbally. Any change in scope, color, schedule or cost is a written change order approved by the board before work starts.

Everything is logged. Calls, emails, decisions and complaints go in the project log the same day.
